


Delivery Note

Framing package for Lot 14, drop 2 of 3: wall framing, sheathing and hardware.

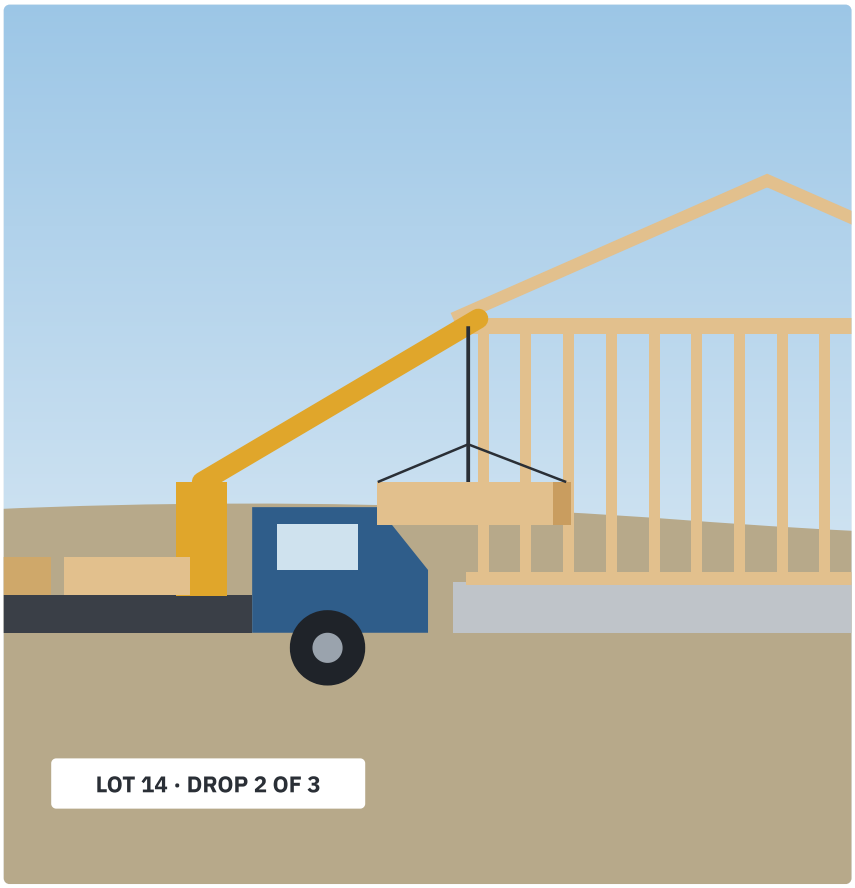

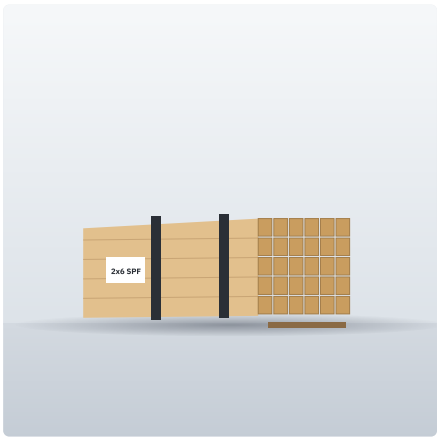

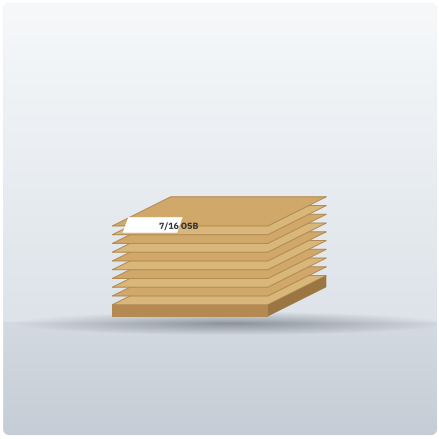

DELIVERY NOTE # RLS-DN-104772
DATE Oct 5, 2027
DELIVERY DATE Oct 5, 2027

SUPPLIER
Ridgeline Lumber & Supply
Cody Marsh
+1 208 555 0117
dispatch@ridgelinelumber.example

DELIVER TO
Sawtooth Homes LLC
Brian Teller
+1 208 555 0162
brian@sawtoothhomes.example
Customer PO: SH-PO-1188

This delivery

Delivered by boom truck and set where the framing crew asked, on dunnage off the dirt.

DROP
2 of 3
Walls and sheathing

LOADS
2
Boom trucks 12 and 15

WEIGHT
21,400 lb
Total, both loads

ARRIVED
7:20 am
Oct 5, 2027

UNLOADED
8:35 am
No crane needed

RECEIVED BY
B. Teller
Site superintendent

Items shipped

Quantities against customer PO SH-PO-1188. Items to follow come on drop 3.

ITEM	ORDERED	SHIPPED	TO FOLLOW
2x6 SPF precut stud, 104-5/8 in	620	620	0
2x6 SPF #2, 16 ft	140	140	0
2x6 pressure-treated sill plate, 16 ft	24	24	0
LVL header 1-3/4 x 11-7/8 in, 12 ft	6	6	0
7/16 in OSB wall sheathing, 4 x 8	180	180	0
7/16 in OSB roof sheathing, 4 x 8	120	0	120
Hurricane ties, galvanized	220	150	70
Framing nails, 16d, coil, box	6	6	0
House wrap, 9 x 150 ft roll	4	4	0

Made with ExtraflowDoc

extraflowdoc.com

Bundles and where they were set

Every bundle is tagged with this delivery note number and its bundle number.

BUNDLE	CONTENTS	SET AT
1–4	Precut studs, 155 per bundle	North side of the slab
5	2x6 x 16 ft and sill plate	North side of the slab
6	LVL headers	Garage slab, on dunnage
7–9	Wall OSB, 60 sheets per unit	East side, tarped
10	Hardware, nails and house wrap, on a pallet	In the job trailer

Still to come

ITEM	QUANTITY	PLANNED
Roof trusses, per the truss layout	1 set	Drop 3, Oct 19
7/16 in OSB roof sheathing	120	Drop 3, Oct 19
Hurricane ties, back-ordered	70	Drop 3, Oct 19
OSB to replace damaged sheets	3	Drop 3, Oct 19

Made with ExtraflowDoc

extraflowdoc.com

Checked at delivery

Checked by the driver and the site superintendent together before signing.

Counts

☑ Bundle tags match this delivery note

☑ Sheet counts on OSB units confirmed

☑ Hardware pallet counted against the list

Condition

☑ Lumber dry and straight, no splits over grade

☐ OSB: 3 sheets with crushed corners, noted below

☑ Bundles set level on dunnage, tarped

Exceptions

Noted on site and signed by both parties.

ITEM	PROBLEM	WHAT HAPPENS
Hurricane ties	70 short, back-ordered	Ship on drop 3; invoiced when shipped
Wall OSB	3 sheets with crushed corners	Kept for blocking; 3 replaced at no charge

Made with ExtraflowDoc extraflowdoc.com

Delivery terms

1. Ownership and risk

1.1 Risk passes to the customer when materials are set on site and this note is signed. Materials stay the supplier's property until the invoice is paid.

2. Claims

2.1 Shortages or damage not noted on this note must be reported within 48 hours, with photos.

3. Returns

3.1 Full, unopened units in resalable condition may be returned within 30 days, picked up for a $75 fee, with a 15% restocking charge on special-order items.

4. Invoice

4.1 Shipped items are invoiced on account at the prices of quote RLS-Q-8840. Items to follow are invoiced when they ship.

Received

Received in good order except as noted under Exceptions.

CUSTOMER SIGNATURE

_____

DATE

_____

FULL NAME

_____

POSITION

_____

Made with ExtraflowDoc

extraflowdoc.com
